

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	02 OCTOBER 2026
Team ID	SWTID-2026-5741
Project Name	IMPORT DATA USING TRANSFORM MAPS(Spreadsheet)
Maximum Marks	5 Marks

Velocity: Velocity:

Planning rules: Sprint = 6 days. Epic = large work split into Stories. Story Points: 1, 2, 3, 5 (very easy to difficult). Sprint dates, completed points and the burndown line are sample values – replace them with your real data.

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Data Preparation	USN-1	Prepare the source Excel / CSV file with clean headers	2	High	[Name]
Sprint-1		USN-2	Check dates, choices and e-mail formats	3	High	[Name]
Sprint-1	Data Loading	USN-3	Create Data Source and upload file using Load Data	3	High	[Name]

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1		USN-4	Load data into the import set (staging) table	3	High	[Name]
Sprint-1		USN-5	Review staged rows before transforming	2	Medium	[Name]
Sprint-2	Transform Map Configuration	USN-6	Create transform map (source → target)	3	High	[Name]
Sprint-2		USN-7	Auto Map Matching Fields	2	High	[Name]
Sprint-2		USN-8	Manual field maps for different column names	3	High	[Name]
Sprint-2		USN-9	Set coalesce field to avoid duplicates	3	High	[Name]
Sprint-2		USN-10	Map reference fields using lookup value	5	Medium	[Name]
Sprint-3	Transform Execution & Validation	USN-11	Run the transform from the import set	2	High	[Name]

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-3		USN-12	Review Import Log and Transform History	3	High	[Name]
Sprint-3		USN-13	Add onBefore transform script for clean-up	5	Medium	[Name]
Sprint-3		USN-14	Verify records in the target table	2	High	[Name]
Sprint-3		USN-15	UAT sign-off and documentation	3	Medium	[Name]

Project Tracker, Velocity & Burndown Chart (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	13	6 Days	05 Oct 2026	10 Oct 2026	[Update]	[Update]
Sprint-2	16	6 Days	12 Oct 2026	17 Oct 2026	[Update]	[Update]

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-3	15	6 Days	19 Oct 2026	24 Oct 2026	[Update]	[Update]
Total	44	18 Days				

Velocity:

Velocity tells how many story points the team completes in one sprint. Total story points = 13 + 16 + 15 = 44, number of sprints = 3.

Measure	Calculation	Result
Team velocity	Total story points ÷ number of sprints = 44 ÷ 3	14.67 ≈ 15 story points per sprint
Average velocity per day (AV)	Total story points ÷ total days = 44 ÷ 18	2.44 story points per day

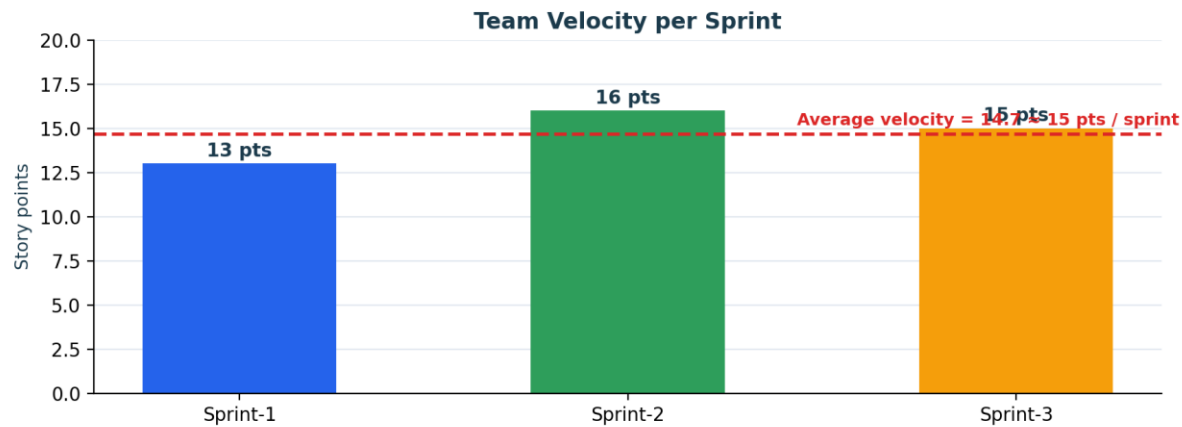


Figure 7: Story points planned per sprint and average velocity

Burndown Chart

A burndown chart is a graphical representation of work left to do versus time. The dashed line is the ideal pace; the green line is the work actually remaining at the end of each day (sample data – update with your own).

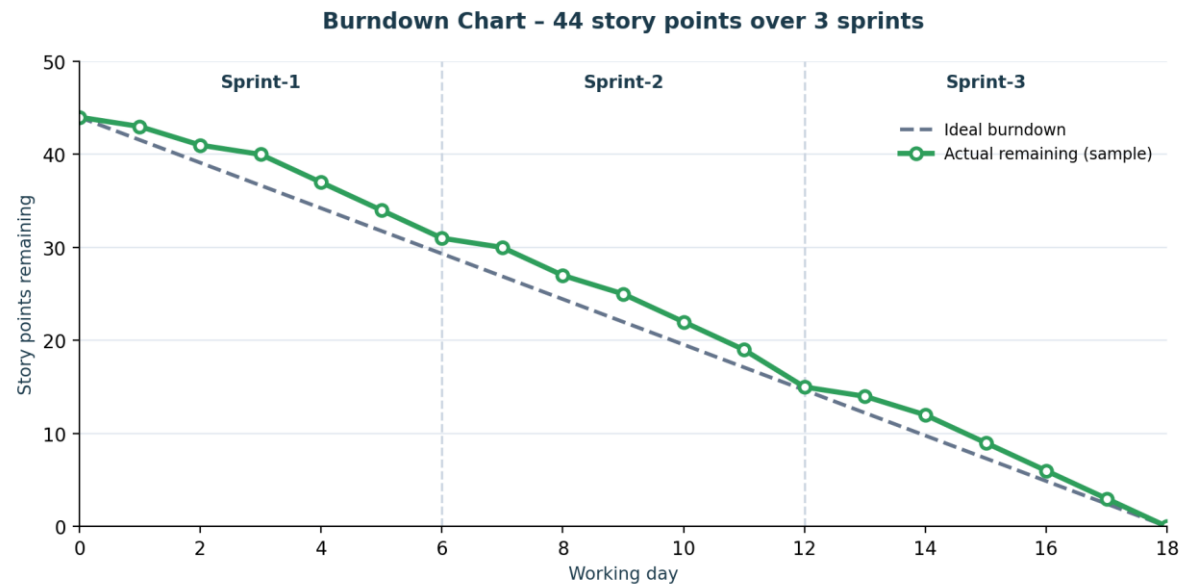


Figure 8: Sprint burndown chart (sample data)

References: <https://www.atlassian.com/agile/tutorials/burndown-charts>

- <https://www.atlassian.com/agile/project-management>
- <https://www.visual-paradigm.com/scrum/scrum-burndown-chart/>
